



III. Master Schedule Report

The modernization projects are divided into five groups and they are scheduled to go to construction as the bond sale cash flow permits. The order of construction delivery of the projects is indicated in the following master schedule.

As of November 15, 2004, the designs for all projects with state funding were complete. We have submitted 51 projects to the State Architects office for review. All school projects are approved by the State Architect's office. All projects have been submitted to the State for funding approval and with the one exception these projects have been approved by the State Allocation Board.

Notice of Completion has been filed on all Group One & Two Projects and 3 Group 3 Projects. Group 3 Projects started construction in mid April 2005 and are at 99% complete. Group 4 construction started in March 2006 and are 55% complete.

The following is a summary of the status of the projects by Group.

Group 1 (DSA Close Out Phase): Mt. Diablo High, Oak Grove MS, Riverview MS, Northgate High, Clayton Valley High, Shore Acres, Willow Creek Center, College Park High, Concord High, Ygnacio Valley High and Eagle Peak Montessori School.

Group 2 (DSA Close Out Phase): Rio Vista ES, Glenbrook MS, Meadow Homes ES, El Monte ES, Bel Air ES, Sun Terrace, ES Cambridge ES, Ygnacio Valley ES, Fair Oaks ES, Olympic High, Mt. Diablo High Increment 2, Mt. Diablo High Shop, and Wren ES

Group 3 (DSA Close Out Phase): Valley View ES, Hidden Valley ES, and Sequoia MS

Group 3 (Contract Close Out Phase): El Dorado MS, Foothill MS, Mt. Diablo ES, Highlands ES, Pine Hollow MS, and Holbrook ES.

Group 4 (Construction Phase): Walnut Acres ES, Pleasant Hill ES, Ayers ES, Monte Gardens ES, Mountain View ES, Sequoia ES, Woodside ES, Valle Verde ES, Valhalla ES, Bancroft ES, Pleasant Hill Ed. Center, and Gregory Gardens ES.


Group 5 (Design complete): Silverwood ES, Westwood ES, Strandwood ES, Sunrise Center, Shadelands Center, and Willow Creek Center.

Group 5 (Design Phase/ DSA review): Diablo View ES, Central Services, Dent Center, Willow Creek Phase 2 and Loma Vista Center.

Overall, the District is meeting the schedule for delivery of the project designs and construction.



MDUSD Measure C Program Master Schedule

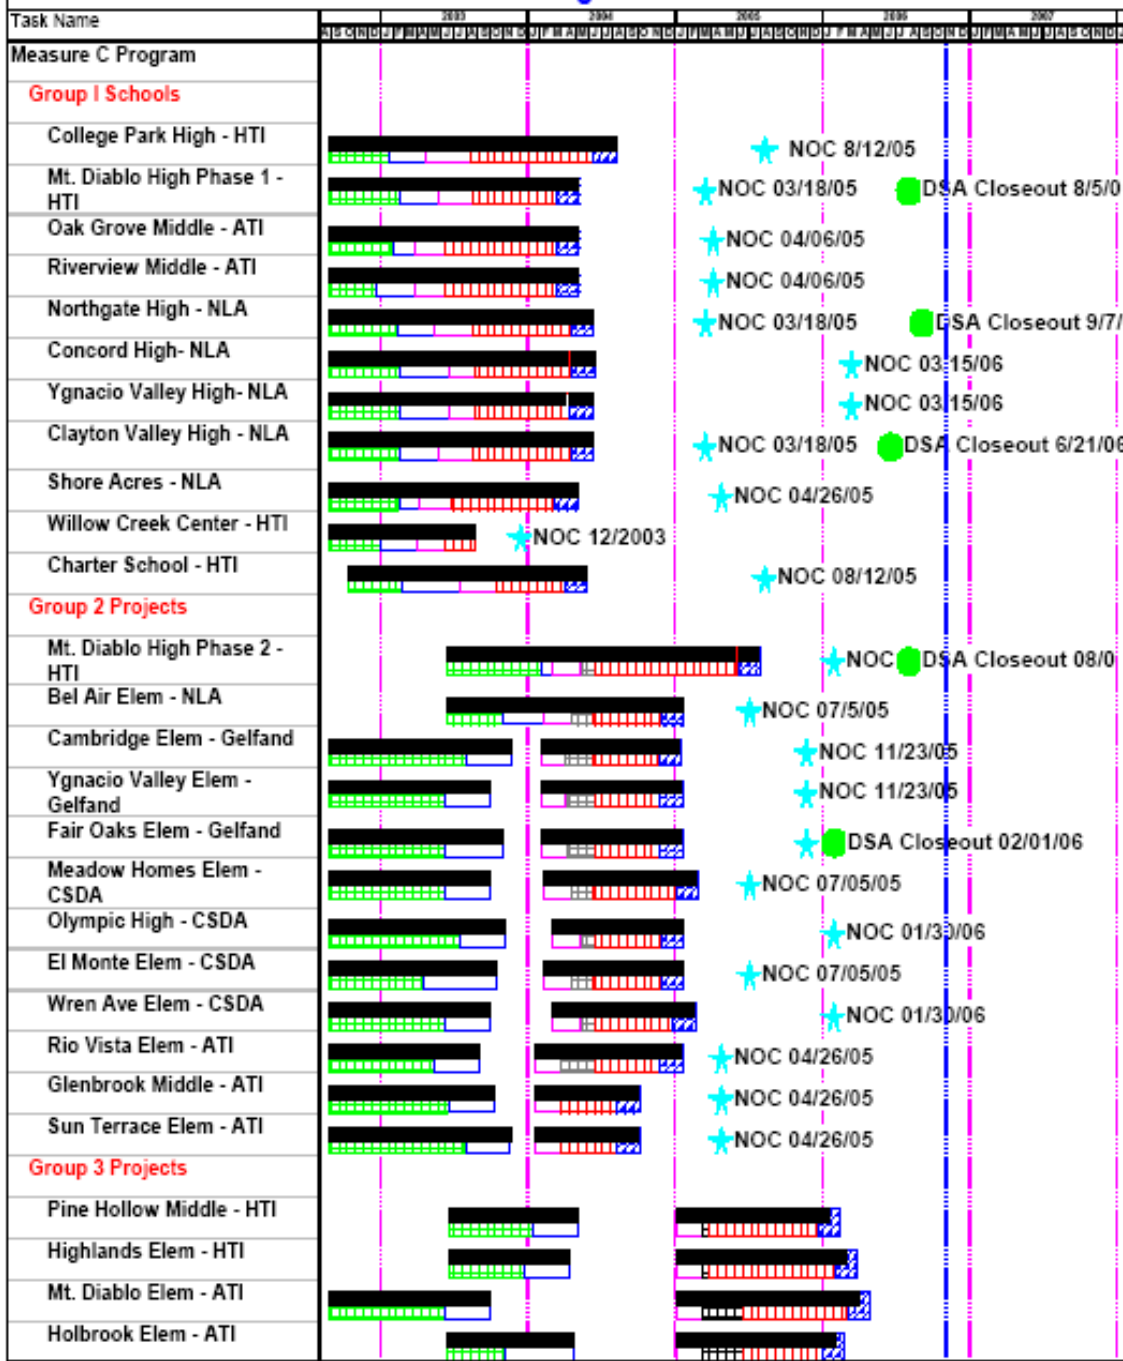

LEGEND ::



